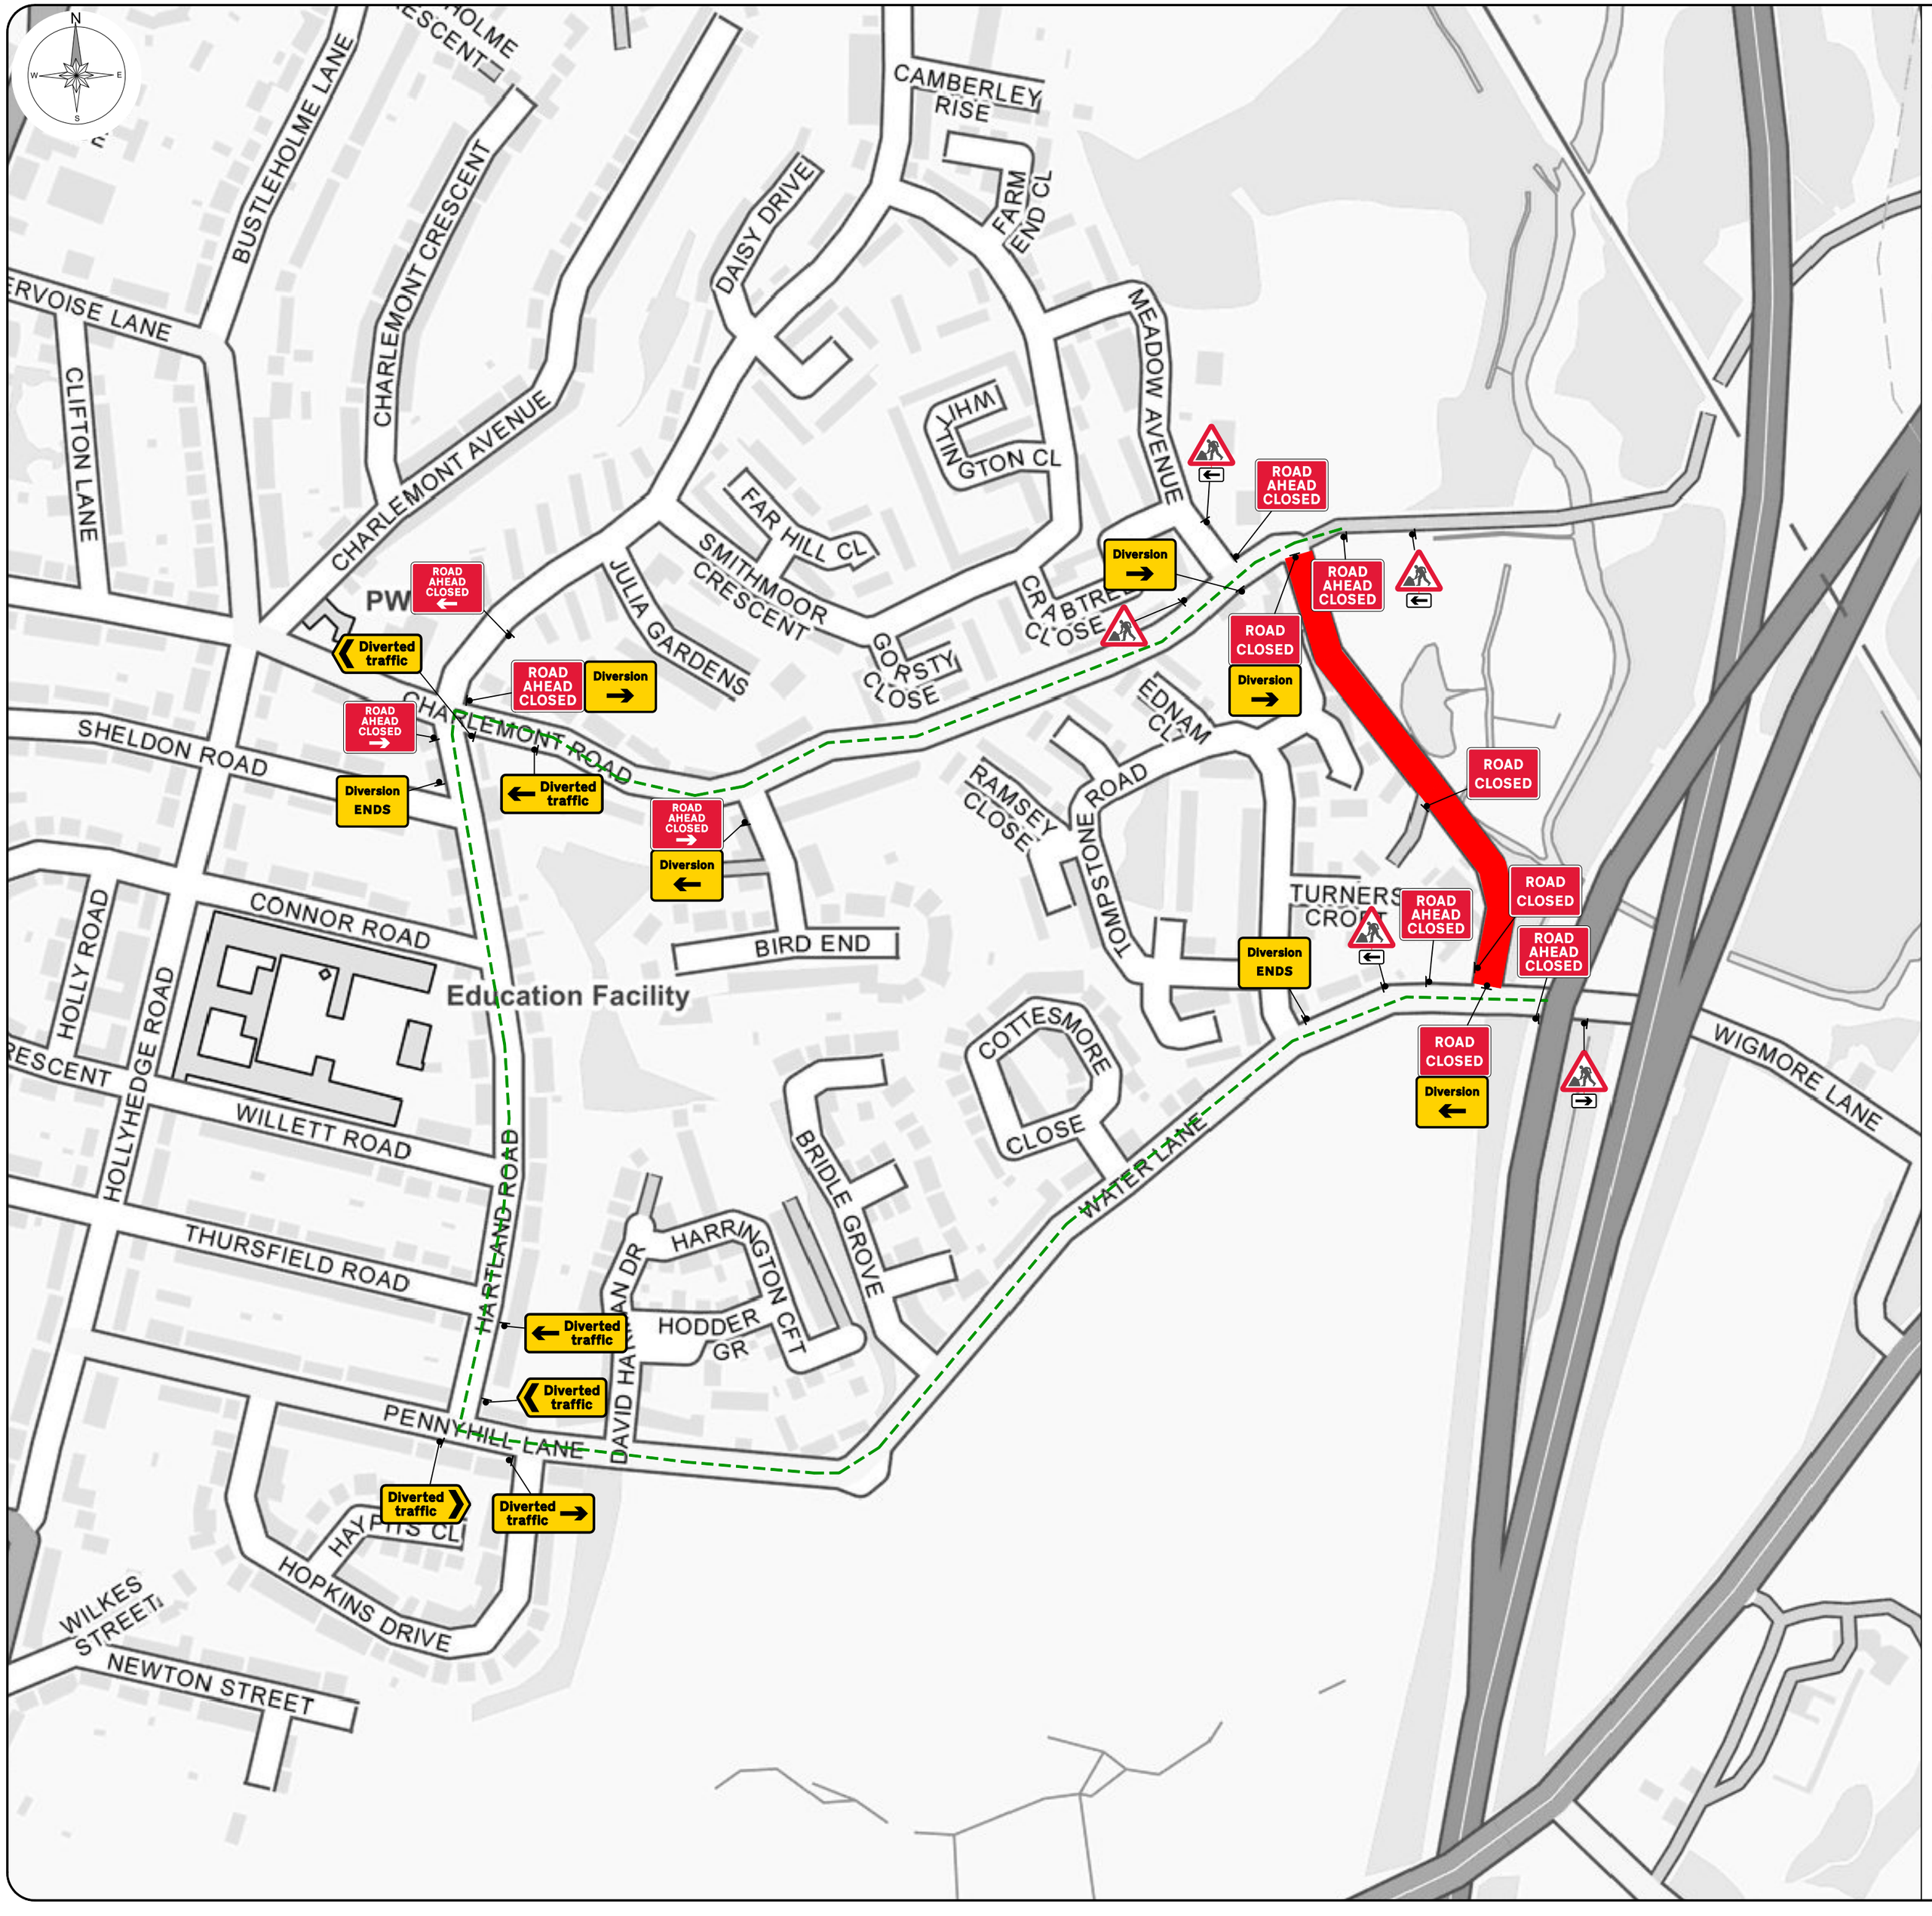

Desktop survey undertaken from google street view with imagery dated: May 2016

All traffic management shall comply with all current legislation and guidance including Chapter 8, Safety at Street Works and Road Works (A Code of Practice).

Pedestrian management to be installed and managed to suit site conditions in accordance with current legislation & codes of practice by the contractor unless otherwise stated.

All signage and road markings shall conform with the Traffic Signs Regulations and General Directions (TSRGD).

Sign locations are indicative only, exact location to be determined on site.

Suitably qualified operative to assess site to ensure the installation complies with all current legislation. Any issues and/or changes from the original design should be immediately reported to the relevant contracts manager/designer.

This design is only valid for 12months from date of production and should be re-evaluated if installation is to take place after this period.

SIGN SCHEDULE

Qty: 3 Ref: 13-9 Schedule 13-9 : Temporary Information	ROAD AHEAD CLOSED →
Qty: 3 Ref: 2702 Start of temporary diversion route	Diversion →
Qty: 2 Ref: 2702 End of temporary diversion route	Diversion ENDS
Qty: 2 Ref: 2702 Start of temporary diversion route	Diversion ←
Qty: 2 Ref: 2703 Direction of temporary diversion route from junction ahead	← Diverted traffic
Qty: 1 Ref: 2703 Direction of temporary diversion route from junction ahead	Diverted traffic →
Qty: 2 Ref: 2704 Direction of temporary diversion route	← Diverted traffic
Qty: 1 Ref: 2704 Direction of temporary diversion route	Diverted traffic →
Qty: 3 Ref: 573 Direction to hazard-left	←
Qty: 1 Ref: 573 Direction to hazard-right	→
Qty: 5 Ref: 7001 Road works ahead	
Qty: 5 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Ahead Closed	ROAD AHEAD CLOSED
Qty: 4 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Closed	ROAD CLOSED

AWS signage installed at least 2 weeks prior to works commencing. Dates & durations to be confirmed.

Road closed XX XXX for X weeks

Key:

	Works Area		Temporary Traffic Signal
	Closure		Stop & Go Board
	Vehicular Diversion Route		Temporary Ped Signal
	Ped Diversion Route		Existing Bus Stop
	Cone		Temporary Sign
	Datum Point		Pedestrian Barrier

Safety information:

Min width of sideways safety zone (S)	0.5m
Min length of longways clearance (L)	0.5m
Wigmore Lane	30

Site information:

NSG	Wigmore Lane, West Bromwich				
Local Authority	Sandwell				
USRN	33653060				
Road Type	Single lane carriageway		Road Width	Varies	
Works Location	X:402062		Y:293808		
Surveyed	X	Bus Stop(s)	X	Parked Vehicles	X
Perm Signals	X	Controlled Crossing	X	Cycle Lanes	X

Chapter 8 details:

Detail B (B) — 1.5m

Single/Dual carriageway 40mph or less-450mm traffic cones.
Single/Dual carriageway 50mph or more-750mm traffic cones.
Dual carriageway national speed limit - 750mm traffic cones.
relaxation 3m.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
2) 45° tapers have 1.2m spacing, no relaxations.
3) On motorways and NSL AP duals with hard shoulders, 1m cones will be required for both standard and relaxation works for lead tapers and the facing wall of lane changes.

Detail C1 (C1) — 9m

Single/Dual carriageway 40mph or less - 450mm traffic cones.
Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
2) For relaxation to Detail C1 see Table A1.3 (Appendix 1).

Detail C2 (C2) — 3m

Single carriageway 40mph or less - 450mm traffic cones.
Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3.

Rev	Date	Comments	By	Chk
-	-	-	-	-

serco

Working in Partnership with

traffix

total traffic & event management solutions

Old Arden Brickworks | Bickenhill | Solihull |West Midlands | B92 0DY
t +44 (0)800 819 9001 | f +44 (0)1675 442507
info@traffixuk.com | www.traffixuk.com

Project title:
Traffic Management

Drawing title:
Proposed Road Closure
Wigmore Lane
West Bromwich
B71 3TD

Date: 29/03/2026	Scale: NTS	Paper: A2
Drawn: CM	Checked: BN	Approved: MW
Project Number: TFX MW850	Drawing Number: 001	Revision: -

This drawing is copyright & the property of Traffix & must not be copied in whole or in part without their written permission. Copyright is reserved. ©
This drawing must not be scaled.
The Contractor is to report all discrepancies & errors to the Contract Manager prior to works commencing.
