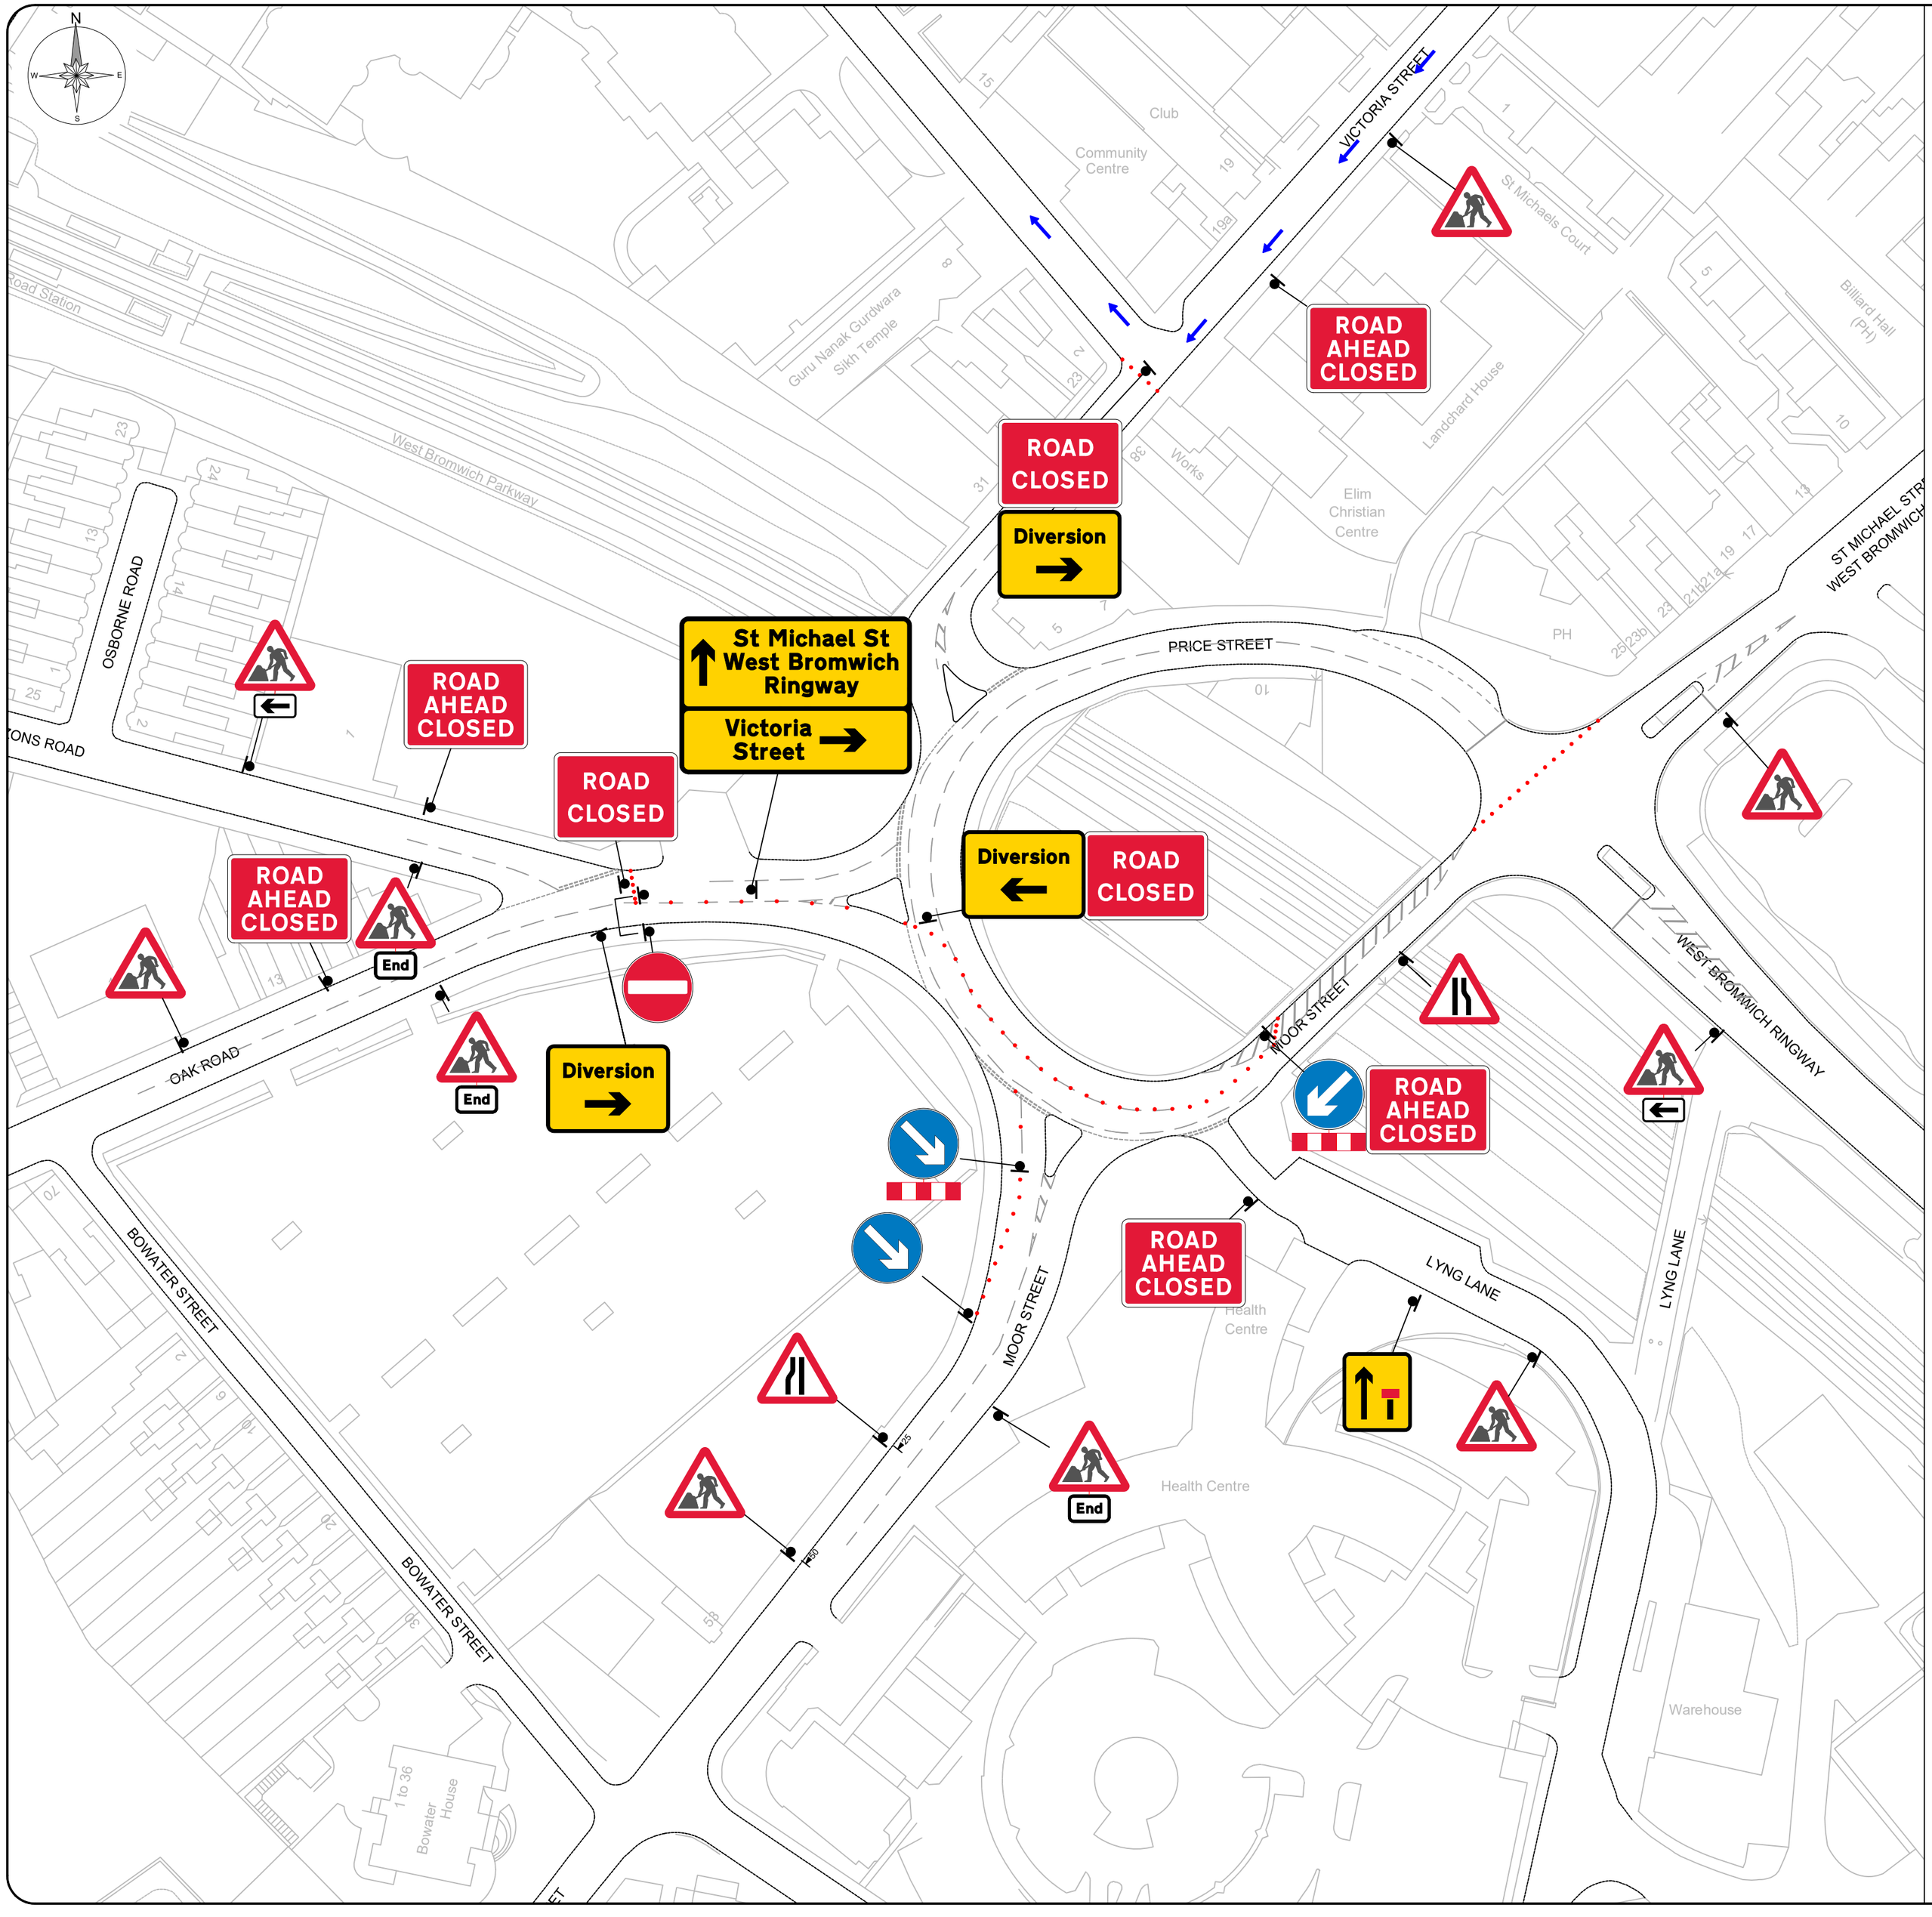


Desktop survey undertaken from google street view with imagery dated: September 2025

All traffic management shall comply with all current legislation and guidance including Chapter 8, Safety at Street Works and Road Works (A Code of Practice).

Pedestrian management to be installed and managed to suit site conditions in accordance with current legislation & codes of practice by the contractor unless otherwise stated.

All signage and road markings shall conform with the Traffic Signs Regulations and General Directions (TSRGD).

Sign locations are indicative only, exact location to be determined on site.

Suitably qualified operative to assess site to ensure the installation complies with all current legislation. Any issues and/or changes from the original design should be immediately reported to the relevant contracts manager/designer.

This design is only valid for 12months from date of production and should be re-evaluated if installation is to take place after this period.

SIGN SCHEDULE

Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	St Michael St West Bromwich Ringway / Victoria Street
Qty: 2 Ref: 2702 Start of temporary diversion route	Diversion →
Qty: 1 Ref: 2702 Start of temporary diversion route	Diversion ←
Qty: 1 Ref: 517 Road narrows on one side only ahead - right	
Qty: 1 Ref: 517 Road narrows on one side only ahead - left	
Qty: 2 Ref: 573 Direction to hazard left	
Qty: 1 Ref: 610 Keep left	
Qty: 2 Ref: 610 Keep right	
Qty: 1 Ref: 616 No entry	
Qty: 3 Ref: 645 End panel	End
Qty: 10 Ref: 7001 Road works ahead	
Qty: 3 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Closed	ROAD CLOSED
Qty: 5 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Ahead Closed	ROAD AHEAD CLOSED
Qty: 2 Ref: 7105 Lane closure barrier	
Qty: 1 Ref: 7202.1 Temporary lane availability	

AWS signage installed at least 2 weeks prior to works commencing. Dates & durations to be confirmed.

Road closed 02 XXX for 3 weeks

Key:

	Works Area		Temporary Traffic Signal
	Closure		Stop & Go Board
	Vehicular Diversion Route		Temporary Ped Signal
	Ped Diversion Route		Existing Bus Stop
	Cone		Temporary Sign
	Datum Point		Pedestrian Barrier

Safety information:	
Min width of sideways safety zone (S)	0.5m
Min length of longways clearance (L)	0.5m
Price Street	30

Site information:					
NSG	Price Street, West Bromwich				
Local Authority	Sandwell				
USRN	33639380				
Road Type	Single lane carriageway	Road Width	Varies		
Works Location	X:400279	Y:291129			
Surveyed	X	Bus Stop(s)	✓	Parked Vehicles	X
Perm Signals	X	Controlled Crossing	X	Cycle Lanes	✓

Chapter 8 details:


Detail B (B)



Single/Dual carriageway 40mph or less-450mm traffic cones.
Single/Dual carriageway 50mph or more-750mm traffic cones.
Dual carriageway national speed limit - 750mm traffic cones.
relaxation 3m.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
2) 45° tapers have 1.2m spacing, no relaxations.
3) On motorways and NSL AP duals with hard shoulders, 1m cones will be required for both standard and relaxation works for lead tapers and the facing wall of lane changes.


Detail C1 (C1)



Single/Dual carriageway 40mph or less - 450mm traffic cones.
Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
2) For relaxation to Detail C1 see Table A1.3 (Appendix 1).

Detail C2 (C2)



Single carriageway 40mph or less - 450mm traffic cones.
Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:
1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3.

Rev	Date	Comments	By	Chk
-	-	-	-	-

Haystoun

Working in Partnership with

traffix

total traffic & event management solutions

Old Arden Brickworks | Bickenhill | Solihull |West Midlands | B92 0DY
t +44 (0)800 819 9001 | f +44 (0)1675 442507
info@traffixuk.com | www.traffixuk.com

Project title:
Traffic Management

Drawing title:
Proposed Road Closure
Price Street
West Bromwich
B70 8EX

Date:	Scale:	Paper:
14/08/2026	NTS	A2
Drawn: CM	Checked: BN	Approved: MT
Project Number: TFX MTH057	Drawing Number: 001	Revision: -

This drawing is copyright & the property of Traffix & must not be copied in whole or in part without their written permission. Copyright is reserved. ©
This drawing must not be scaled.
The Contractor is to report all discrepancies & errors to the Contract Manager prior to works commencing.
